

### Phase 1 | Block C Asbestos Works

- Initial works due to begin in July 2024, with completion due August 2024.
- Phase 1 covers Asbestos removal and the demolition of Block C, which is currently disused temporary classrooms. The affected area of works is to be cordoned off via hoardings for contractor exclusive access.
- Pedestrian and vehicular access to the school site will remain in their current position from Deanstones Lane. Contractor vehicles will access the site via the main entrance.
- There will be no impact to school teaching and facilities at this point, with the works due to be completed during the summer break.

### Block C - Asbestos Works



- KEY:**
- KIERZONE (Green square)
  - BUILD ZONE (Purple square)
  - PROPOSED KIER COMPOUND (Red dashed line with KIER logo)
  - GATES (A,B,C & D) (Red solid line)
  - BUS DROP OFF ZONE (Blue arrow)
  - TRINITY ACADEMY ACCESS / EGRESS (Yellow arrow)
  - KIER CONTRACTORS ACCESS / EGRESS (Red dotted line)
  - KIER VEHICLE ACCESS TO SITE (Blue arrow)

### Phase 2 | Block C Demolition & New Build Construction

- Works due to begin in August 2024, with completion due November 2025.
- Contractor's site compound is to be established on the playing fields to the south of the site, with contractor and delivery access via the main entrance.
- Staff and student pedestrian access to remain via Deanstones Lane. Vehicular access (staff, visitors, bus drop-off) is to be managed by Kier site security.
- External access around the retained Block B and current MUGA locations is to be limited during this period. Internal access to Block B will be via the bridge link from Block A, with fire escape routes via both staircases and the western facade entrance.

### Block C Demo & New Build Sequence





- KEY:**
- KIERZONE (Green square)
  - BUILD ZONE (Purple square)
  - PROPOSED KIER COMPOUND (Red dashed line with KIER logo)
  - GATES (A,B,C & D) (Red solid line)
  - TRINITY ACADEMY ACCESS / EGRESS (Yellow arrow)
  - KIER CONTRACTORS ACCESS / EGRESS (Red dotted line)
  - KIER VEHICLE ACCESS TO SITE (Blue arrow)
  - TRINITY STAFF AND STUDENT FLOW TO AND FROM ASSEMBLE POINT (Yellow arrow)

### Phase 2 | School Access to Retained Building

- External refurbishment works due to begin in July 2024, with completion due December 2024.
- Internal refurbishment works due to begin in July 2024, with six distinct work periods during school holidays. Completion of the internal works is due September 2025.
- Primary student access into the retained Block B is to be via the bridge from Block A to the north. Protected walkways to the perimeter of Block B will allow escape from staircases in case of emergency.
- No school access to the current MUGA area for the whole of the construction duration.

### Refurbishment of Block B During New Build Construction

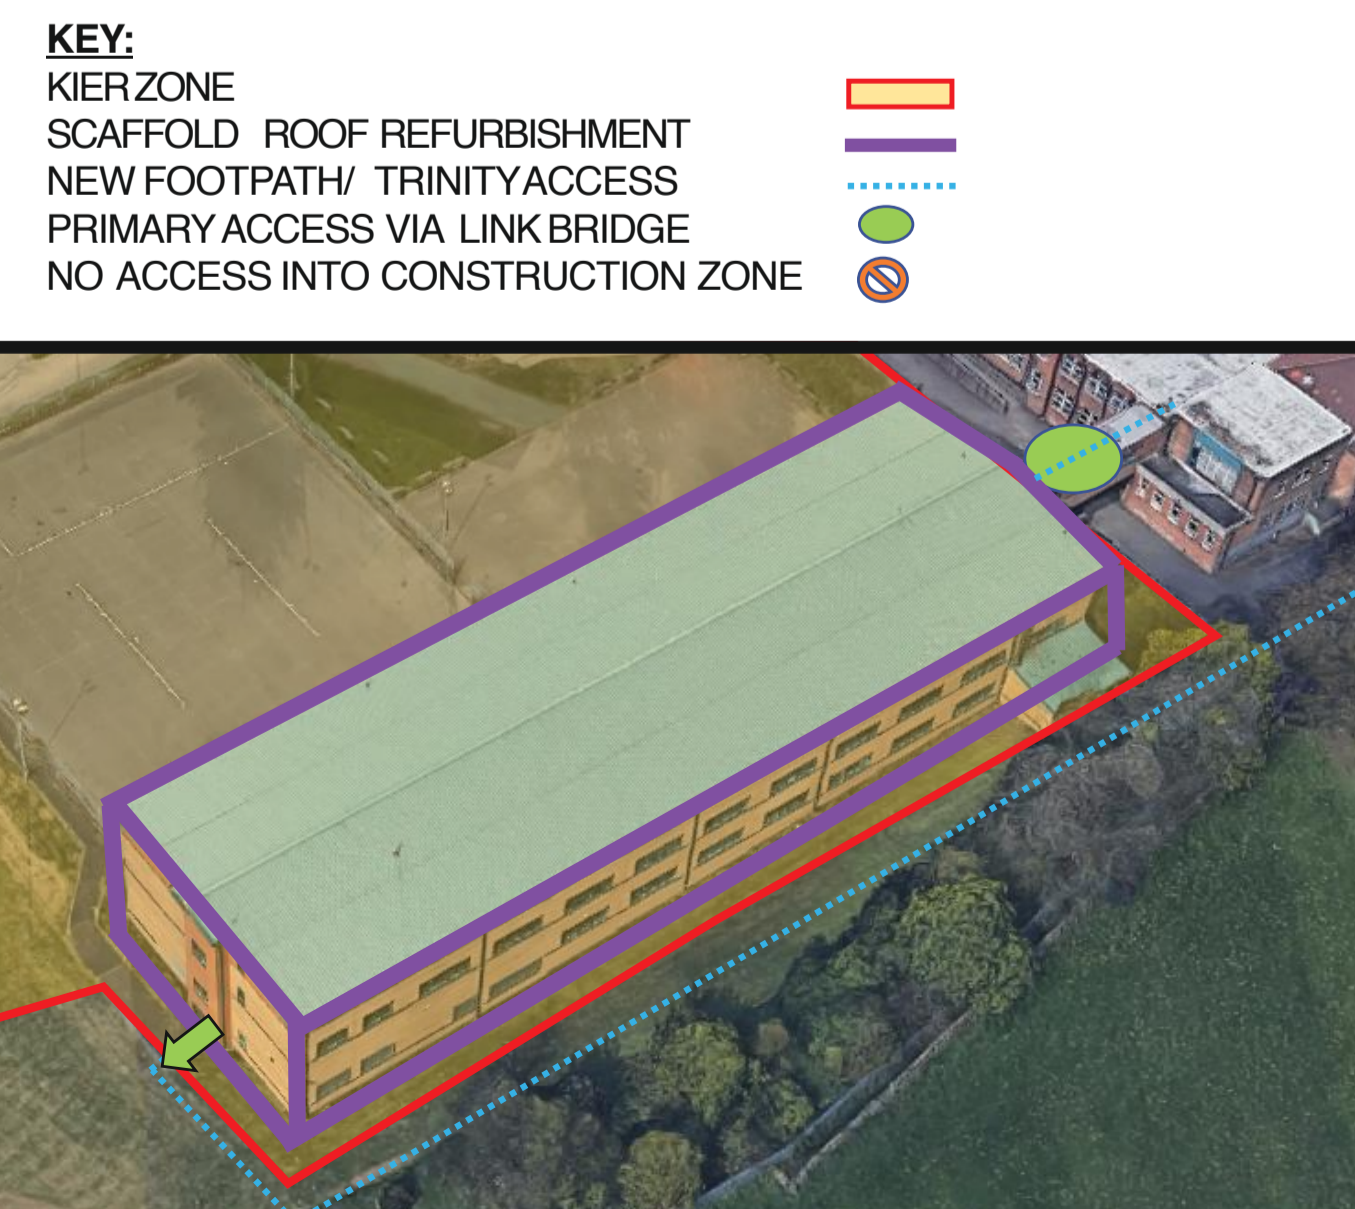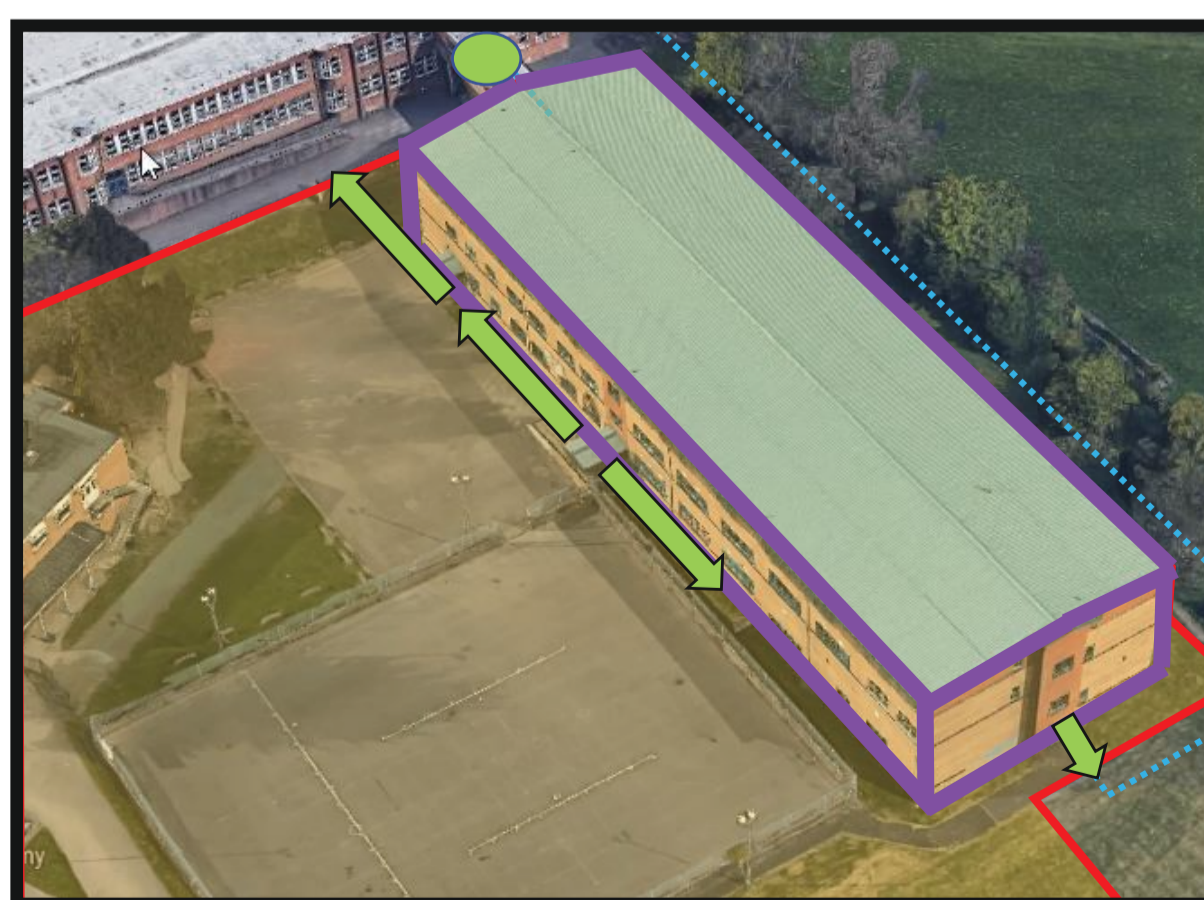

Note: Access from the area denoted with the symbol will be a protected walkway to allow exit outside of Kiers boundary with out any site risks present. The fire strategy with the school is still to be finalised.

### Phase 3 | Block A Asbestos Works and Demolition

- The target for occupation of the new block is due to be November 2025. External works (asbestos survey & removal, demolition of Block A, reinstatement of playing fields) are due to begin in November 2025, and are due for completion in October 2026.
- Contractor's compound is to be established in the north-west corner of the site by Russell Hall Park during this phase. A secure hoarding line to the works area will be established to prevent student access.
- Staff and student access will remain via the main entrance from Deanstones Lane. Contractor access to be via the secondary access from Deanstones Lane to north of the car park. Deliveries will be made via the main entrance, with the process to be managed by Kier.

### Block A - Asbestos & Demo Works



- KEY:**
- KIERZONE (Green square)
  - TRINITY ZONE (Purple square)
  - PROPOSED KIER COMPOUND (Red dashed line with KIER logo)
  - GATE A (Red solid line)
  - BUS DROP OFF ZONE (Blue arrow)
  - TRINITY ACADEMY ACCESS / EGRESS (Yellow arrow)
  - KIER CONTRACTORS ACCESS / EGRESS (Red dotted line)
  - KIER VEHICLE ACCESS TO SITE (Blue arrow)
